

2016 Flood Impacted School Construction Projects





Construction Projects

New Hoover High School


New Clendenin Elementary School



New Hoover High School



New Hoover High School

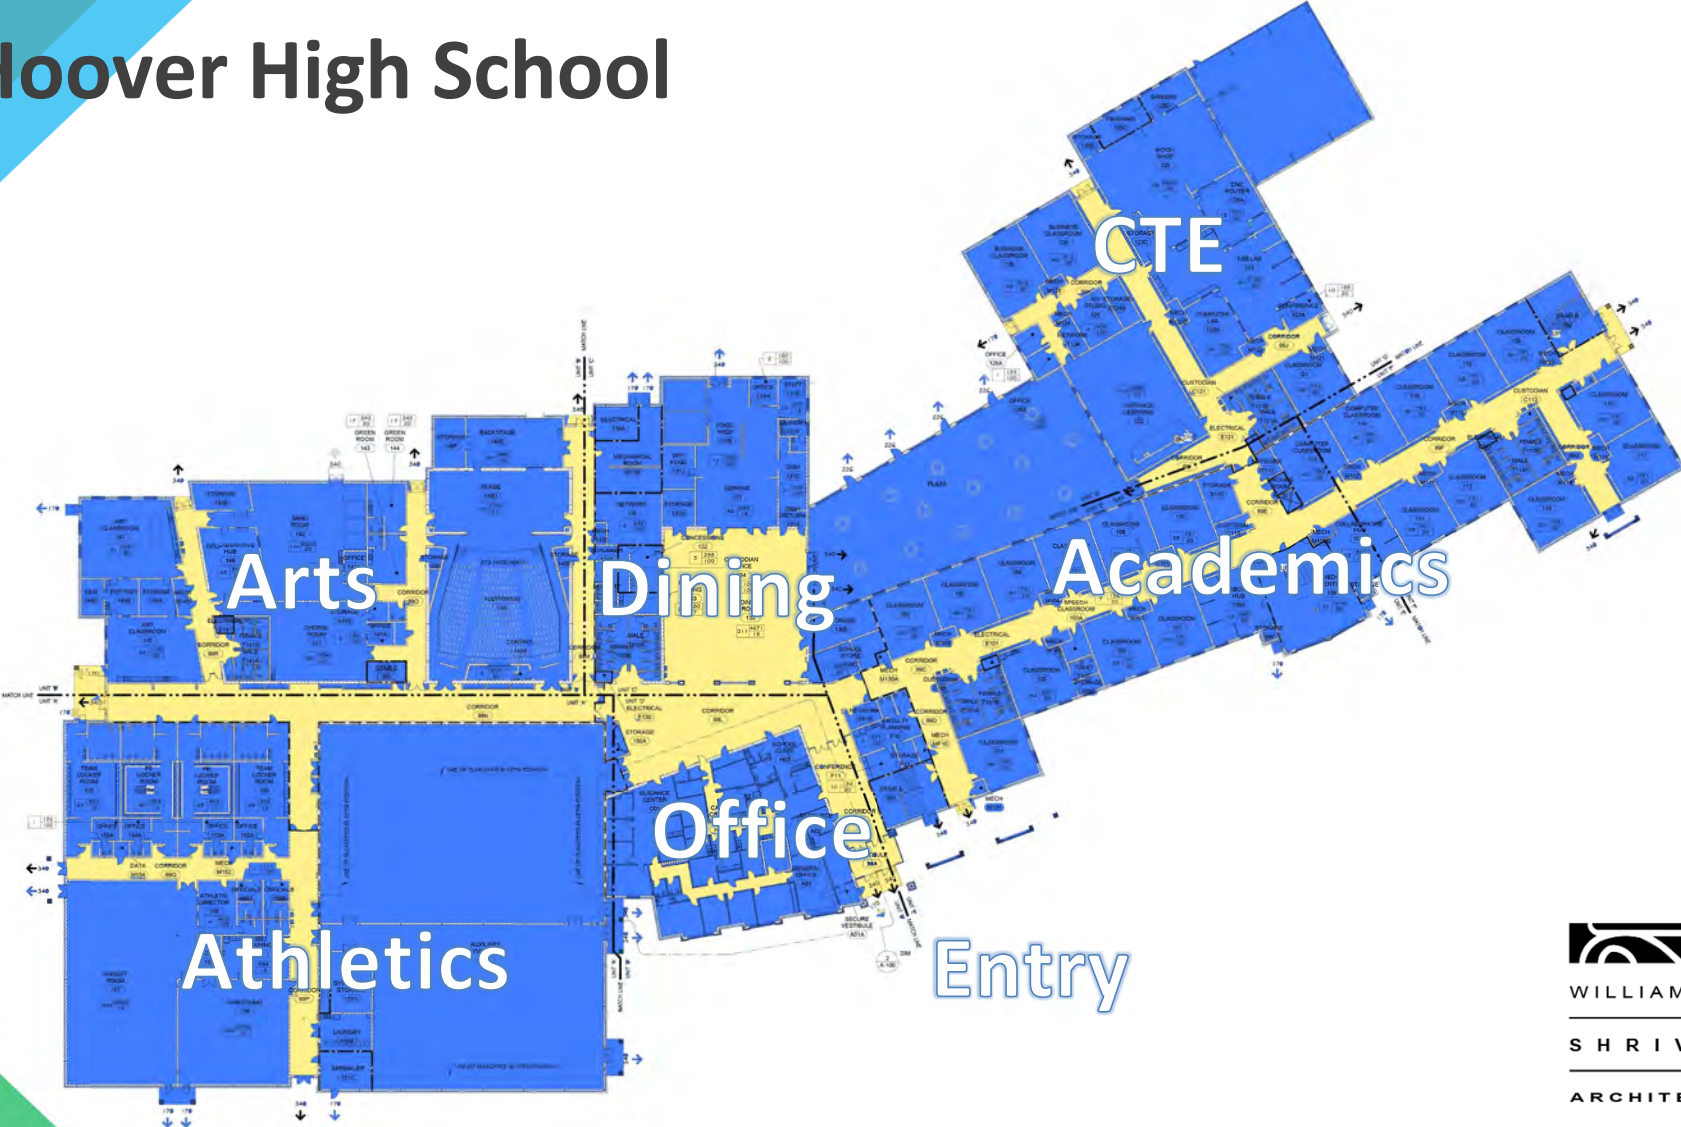

New Hoover High School



New Hoover High School


WILLIAMSON
SHRIVER
ARCHITECTS

ACADEMICS



New Hoover High School


WILLIAMSON
SHRIVER
ARCHITECTS






WILLIAMSON
SHRIVER
ARCHITECTS

New Hoover High School

New Hoover High School



WILLIAMSON
SHRIVER
ARCHITECTS

New Hoover High School



WILLIAMSON
SHRIVER
ARCHITECTS




Construction Timeline

Site Preparation is 98% Complete
Building Construction is 40% Complete
Building Project Completion is Planned
for Late Spring 2023



New Clendenin Elementary

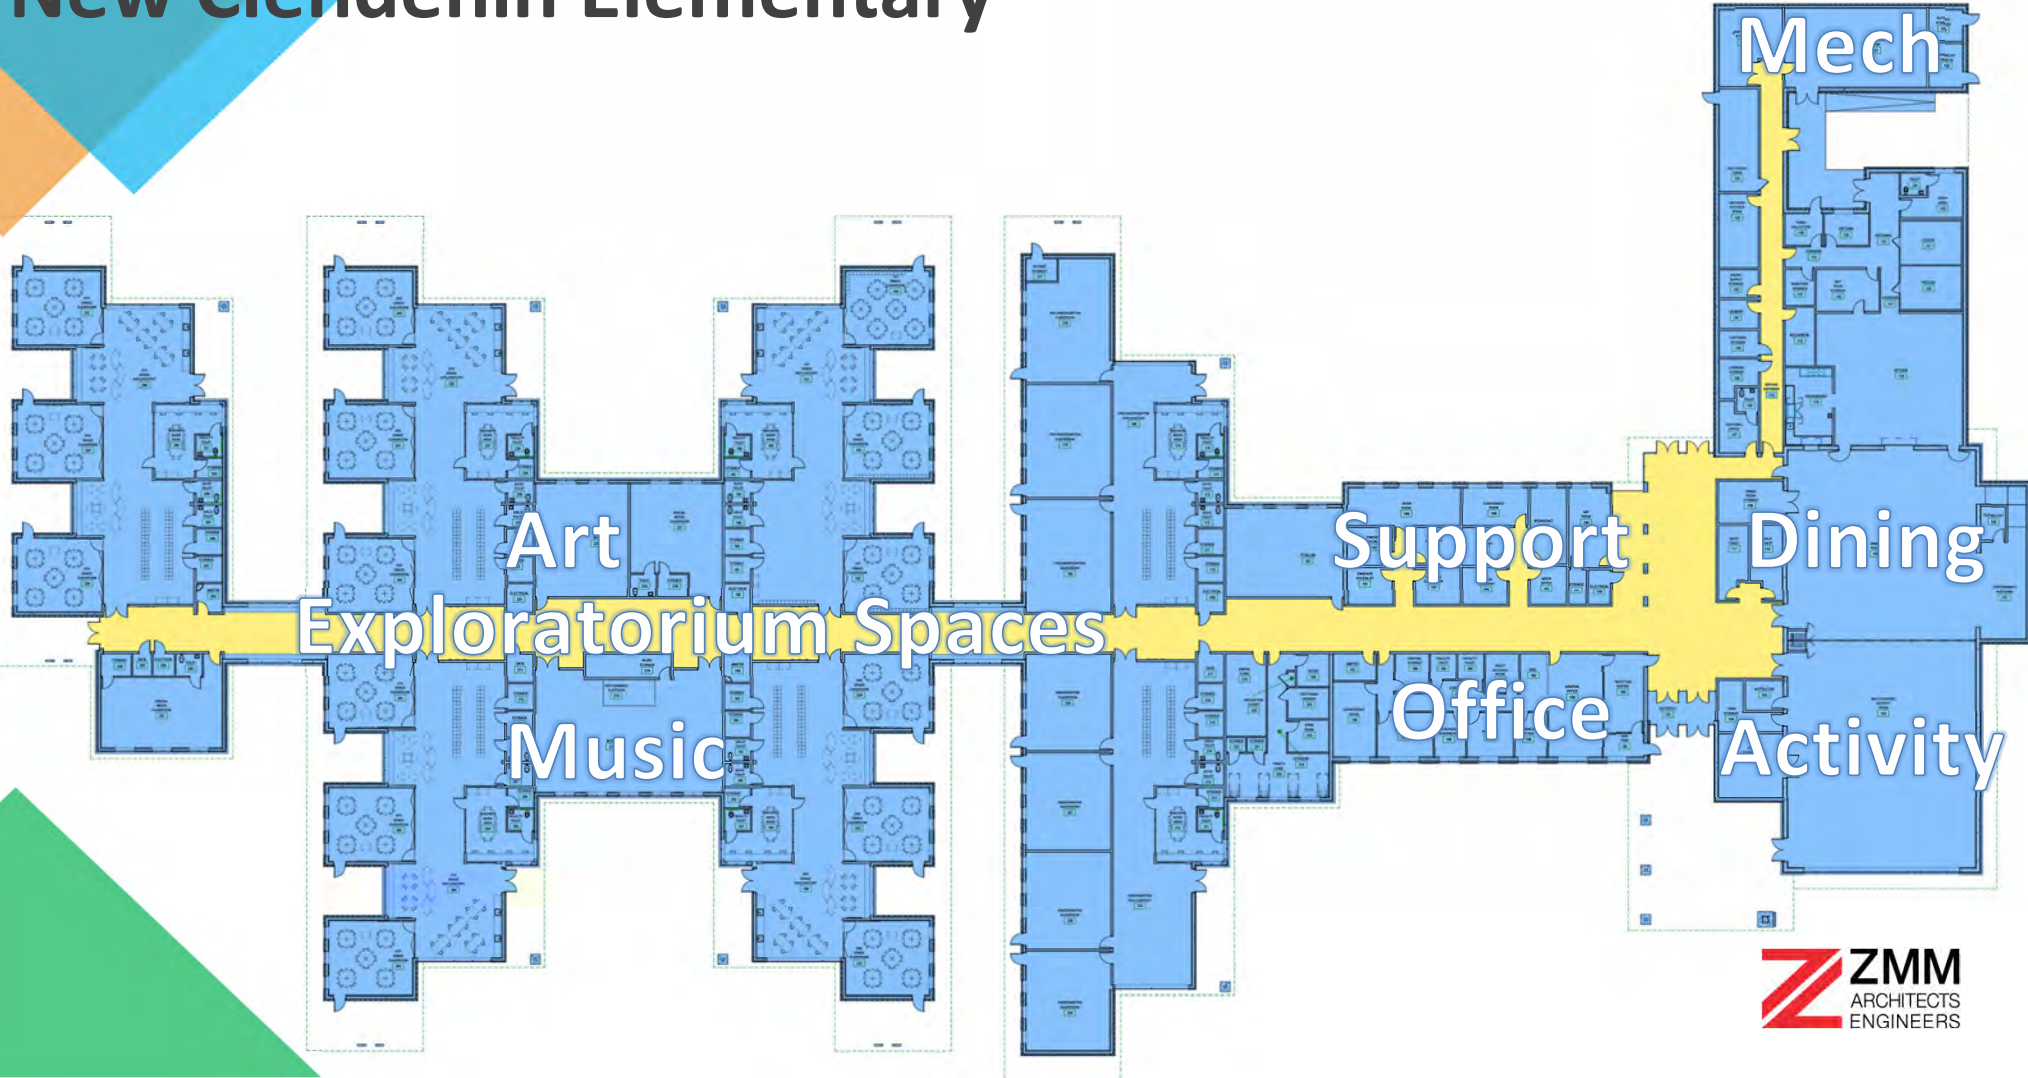



New Clendenin Elementary



New Clendenin Elementary



New Clendenin Elementary

New Clendenin Elementary



New Clendenin Elementary





Construction Timeline

**Construction has started but is on hold.
The project is estimated to take one
year to complete once the Pyritic
Sandstone issue is resolved.**



Construction Projects


**Cherry River Elementary School
Richwood Middle School
Richwood High School**

**Nicholas County High School
Summersville Middle School
NC Career & Technical Center**



CHERRY RIVER ELEMENTARY SCHOOL
RICHWOOD MIDDLE SCHOOL
RICHWOOD HIGH SCHOOL

Site Plan

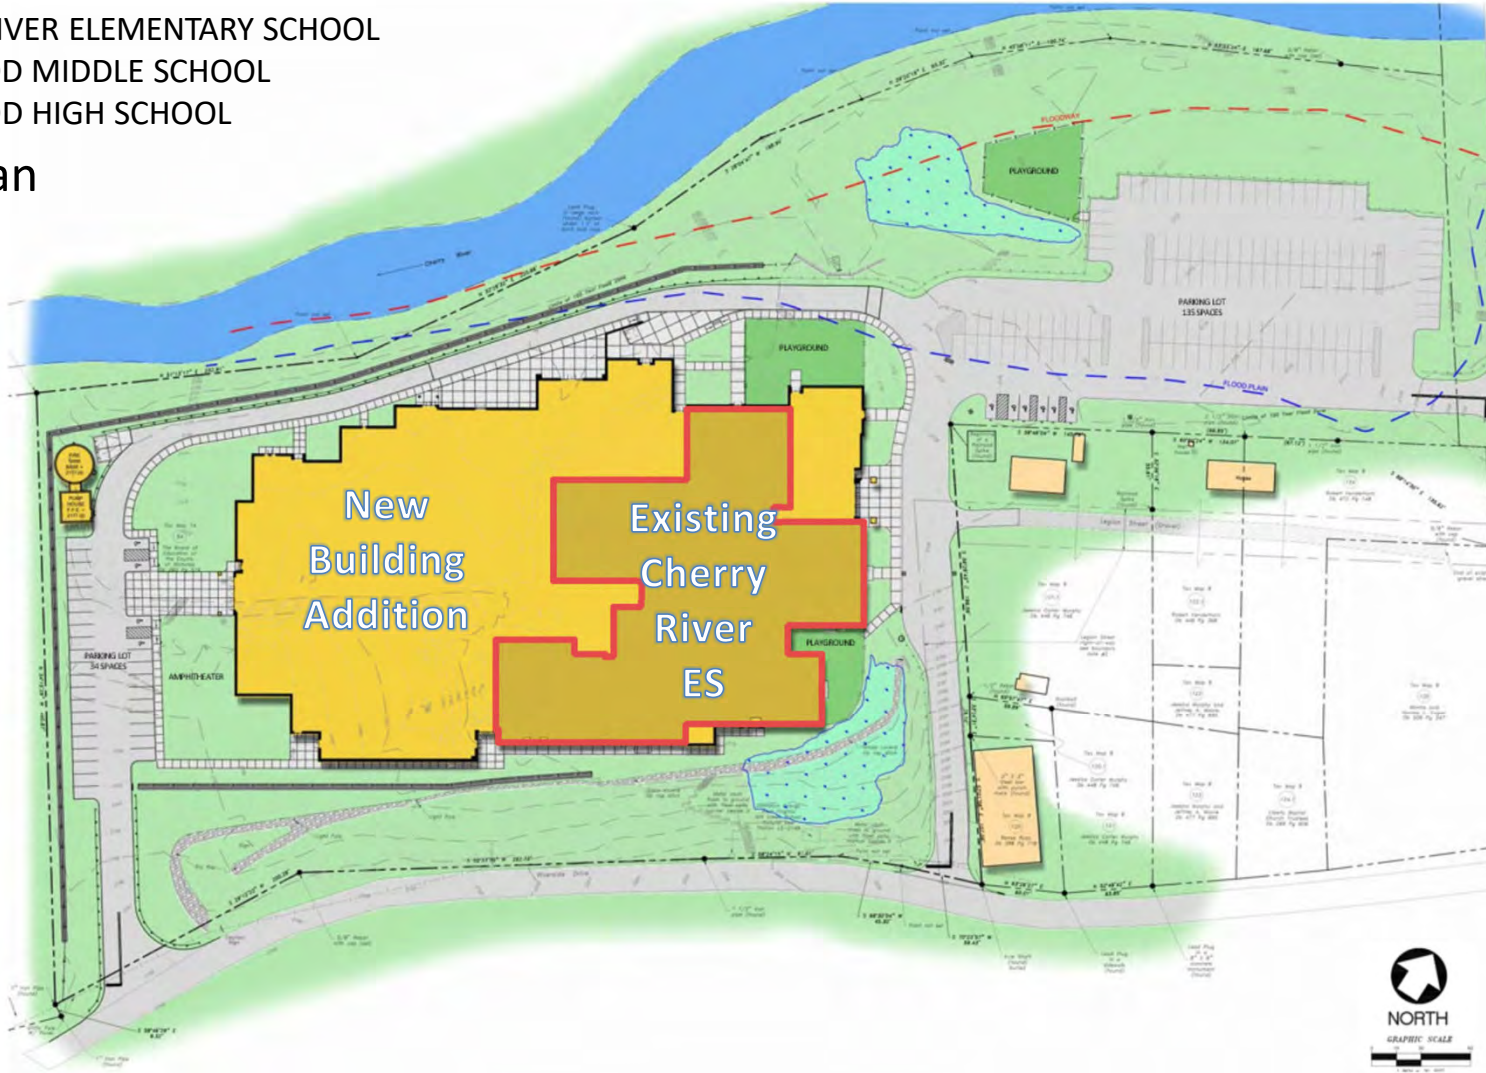

CHERRY RIVER ELEMENTARY SCHOOL
 RICHWOOD MIDDLE SCHOOL
 RICHWOOD HIGH SCHOOL

Floor Plan

Legend

- CIRCULATION
- ELEMENTARY SCHOOL
- HEALTH CLINIC
- HIGH SCHOOL
- MIDDLE SCHOOL
- MULTI-USER SPACES
- SUPPORT SPACES

MS/HS
 Entry



Elementary School Entrance



Middle / High School Entrance



Dining Room





Dining Room



Middle / High School Lobby



Middle / High School Lobby



Elementary School Media Center



**Cherry River Elementary School
Richwood Middle School
Richwood High School**



Construction Timeline

Bids will be opened March 2

Construction to start March 2022


The building will be occupied in phases

Fully occupied by December 2023



SUMMERSVILLE MIDDLE SCHOOL
NICHOLAS COUNTY HIGH SCHOOL
NICHOLAS COUNTY CAREER / TECHNICAL CENTER

Site Plan

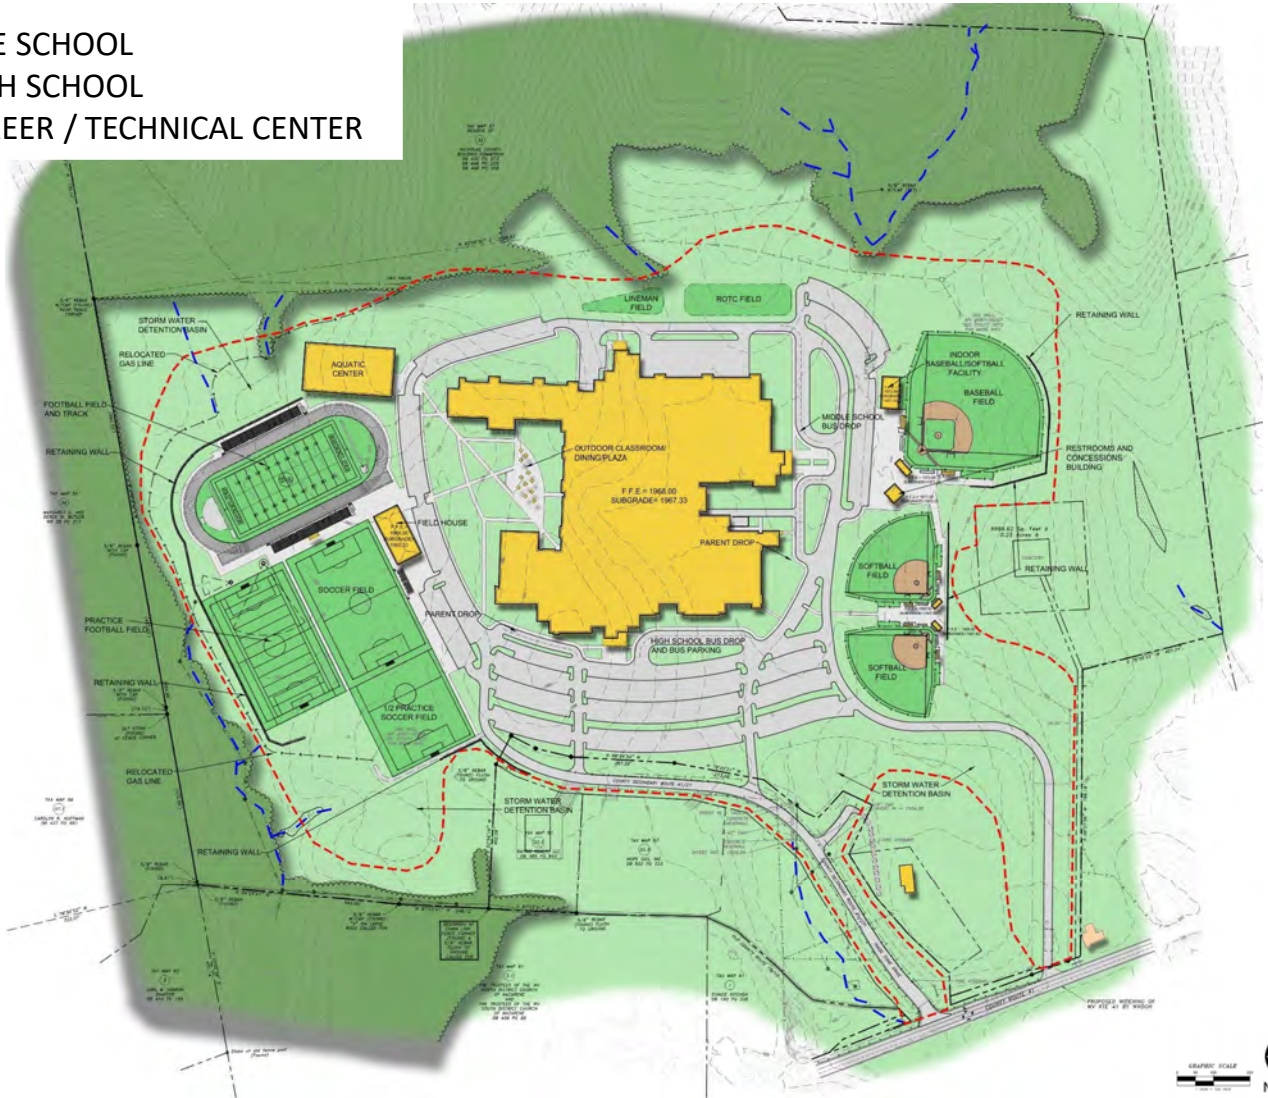

SUMMERSVILLE MIDDLE SCHOOL
 NICHOLAS COUNTY HIGH SCHOOL
 NICHOLAS COUNTY CAREER / TECHNICAL CENTER

First Floor Plan

Academies

- Animal Science
- ProStart
- Cosmetology

Academies

- Auto Tech/Collision
- Welding
- Building Trades



MS Academies

Academies

- Business
- Health
- Engineering
- Journalism

Dining

MS Arts

HS Arts

Athletics

HS Entry

MS Entry



Nicholas County High School
Summersville Middle School

Main Building Entrance





**Nicholas County High School
Summersville Middle School**

Main Building Entrance



Nicholas County High School
Summersville Middle School

Middle School Entrance



Nicholas County High School
Summersville Middle School

Main Entrance Lobby





**Nicholas County High School
Summersville Middle School**

Academy Entrances





**Nicholas County High School
Summersville Middle School**

Looking Towards Entrance Lobby





**Nicholas County High School
Summersville Middle School**

Typical Academy





**Nicholas County High School
Summersville Middle School
NC Career & Technical Center**



Planned Construction Timeline
Building Bids Planned for June 2022
Building Construction to start July 2022
Fully occupied by October 2024





Thank You!

